ID	Task Name	Duration	Start	Finish	Predecessors
1	**ATLAS boards**	**135 days**	**Fri 9/4/99**	**Fri 15/10/99**	
2	*Collaboration board*	0 days	Fri 11/6/99	Fri 11/6/99	
3	*Collaboration board*	0 days	Thu 16/9/99	Thu 16/9/99	
4	Executive board	0 days	Fri 9/4/99	Fri 9/4/99	
5	Executive board	0 days	Wed 2/6/99	Wed 2/6/99	
6	Executive board	0 days	Fri 16/7/99	Fri 16/7/99	
7	Executive board	0 days	Wed 8/9/99	Wed 8/9/99	
8	Executive board	0 days	Fri 15/10/99	Fri 15/10/99	
9	**Overall ATLAS**	**171 days**	**Thu 11/3/99**	**Thu 4/11/99**	
10	Nominate/search coordinators	18 days	Mon 15/3/99	Wed 7/4/99	
11	CB (e-mail) endorse co-ordinators	25 days	Thu 8/4/99	Wed 12/5/99	10
12	Appoint PL for core s/w	0 days	Fri 23/7/99	Fri 23/7/99	24SS
13	Appoint QC group	0 days	Fri 9/4/99	Fri 9/4/99	4
14	QC group work	150 days	Fri 9/4/99	Thu 4/11/99	13
15	First QC recommendations at place	0 days	Thu 17/6/99	Thu 17/6/99	14SS+50 days
16	Overall rec/sim/dBase coordinators appo	0 days	Tue 18/5/99	Tue 18/5/99	31
17	ATLAS overall rec/sim/dBase groups ac	100 days	Tue 8/6/99	Mon 25/10/99	16,32
18	Set up national board	50 days	Fri 11/6/99	Thu 19/8/99	2
19	Set up regional working group	25 days	Fri 20/8/99	Thu 23/9/99	18
20	Taskforce on architecture, initial membe	146 days	Fri 9/4/99	Sun 31/10/99	4
21	Some system coordinators/task leaders	0 days	Mon 7/6/99	Mon 7/6/99	32
22	Architecture defined version 1	0 days	Thu 22/7/99	Thu 22/7/99	20SS+75 days
23	s/w WP template ready	0 days	Thu 22/7/99	Thu 22/7/99	15,20SS+75 days
24	Partition core computing in WP	75 days	Fri 23/7/99	Thu 4/11/99	22,23
25	Negotiate committments on core s/w	50 days	Fri 27/8/99	Thu 4/11/99	18,24SS+25 days
26	Get national training contacts	25 days	Thu 11/3/99	Wed 14/4/99	
27	Set up training information system and p	50 days	Thu 11/3/99	Wed 19/5/99	
28	Set up C++/OO consultancy group	25 days	Thu 15/4/99	Wed 19/5/99	26
29	Computing steering group in place	0 days	Mon 7/6/99	Mon 7/6/99	11,16,32
30	**System activities**	**172 days**	**Wed 10/3/99**	**Thu 4/11/99**	
31	Appoint overall/rec/sim/dBase coordinat	50 days	Wed 10/3/99	Tue 18/5/99	
32	Sceduled coordinator training	5 days	Tue 1/6/99	Mon 7/6/99	
33	Partition system computing in WP	75 days	Fri 23/7/99	Thu 4/11/99	22,23
34	Negotiate in systems on committments	50 days	Fri 27/8/99	Thu 4/11/99	33SS+25 days

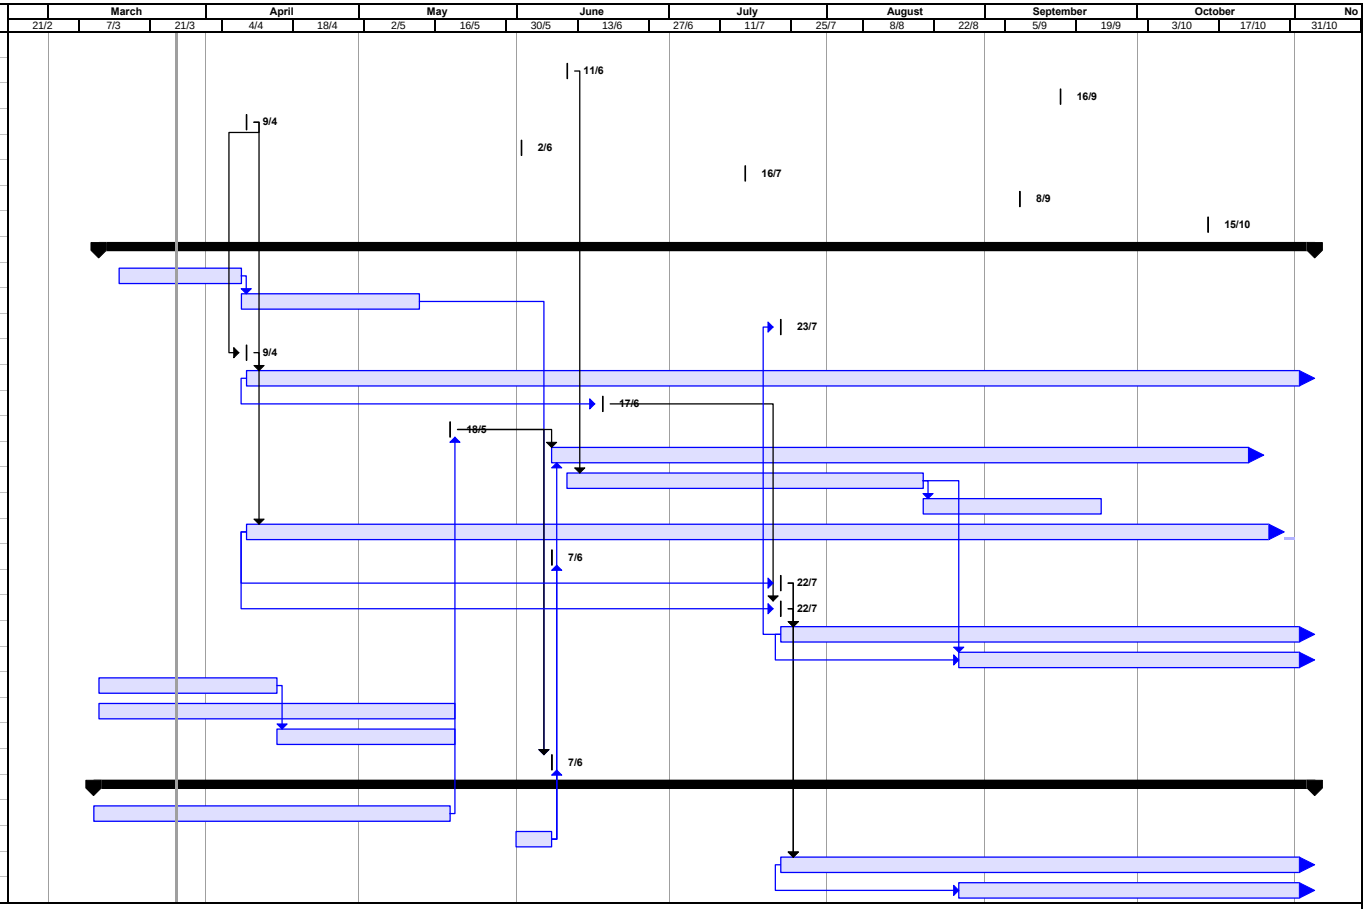

Project: Computing Action Plan: PRELI
Date: Fri 26/3/99

Task | Milestone | Rolled Up Task | Rolled Up Progress | Project Summary | Rolled Up Split
Progress | Summary | Rolled Up Milestone | External Tasks | Split
